

LA-UR-12-26190

Approved for public release; distribution is unlimited.

Title: Los Alamos National Laboratory and Lawrence Livermore National Laboratory Plutonium Sustainment Monthly Program Report October 2012

Author(s): (b) (6)

Intended for: Report



Disclaimer:
Los Alamos National Laboratory, an affirmative action/equal opportunity employer, is operated by the Los Alamos National Security, LLC for the National Nuclear Security Administration of the U.S. Department of Energy under contract DE-AC52-06NA25396. By approving this article, the publisher recognizes that the U.S. Government retains nonexclusive, royalty-free license to publish or reproduce the published form of this contribution, or to allow others to do so, for U.S. Government purposes. Los Alamos National Laboratory requests that the publisher identify this article as work performed under the auspices of the U.S. Department of Energy. Los Alamos National Laboratory strongly supports academic freedom and a researcher's right to publish; as an institution, however, the Laboratory does not endorse the viewpoint of a publication or guarantee its technical correctness.

UNCLASSIFIED

LANL Executive Summary.....	5
Table 1: October Baseline Change Requests	5
1.0 LANL - Pit Development.....	9
1.1 Technical Progress.....	10
1.2 Equipment	10
1.3 Issues	10
1.4 Variance Analysis and Recovery Plan.....	10
1.5 BCRs.....	10
1.6 Earned Value Metrics	11
2.0 LANL - Power Supply.....	12
2.1 Technical Progress.....	12
2.2 Equipment	13
2.3 Issues	13
2.4 Variance Analysis and Recovery Plan.....	13
2.5 BCRs.....	13
2.6 Earned Value Metrics	14
3.0 Program Management and Support.....	15
3.1 Program Management	15
3.2 Support	15
3.3 Issues	15
3.4 Variance Analysis and Recovery Plan.....	15
3.5 BCRs.....	15
3.6 Earned Value Metrics	16
4.0 Facilities, Waste and Institutional Support.....	17
4.1 Technical Progress.....	17
4.2 Equipment	17
4.3 Issues	17
4.4 Variance Analysis and Recovery Plan.....	17
4.5 BCRs.....	17
4.6 Earned Value Metrics	18
5.0 KCP.....	19
5.1 Technical Progress.....	19
5.2 Equipment	19
5.3 Issues	19
5.4 Variance Analysis and Recovery Plan.....	19
5.5 BCRs.....	19
5.6 Earned Value Metrics	20
6.0 LLNL	21
6.1 Technical Progress.....	21
6.2 Equipment	21

6.3 Issues	21
6.4 Variance Analysis and Recovery Plan.....	21
6.5 BCRs.....	21
6.6 Earned Value Metrics	22

LANL Executive Summary

In October of 2012 the Plutonium Sustainment program at LANL completed or addressed the following high-level activities:

- 1) Completed Pollux shipment to DAF in early October in accordance with the Gemini Core Team's schedule. Unpacked Pollux at DAF and supported Gemini team in various tests and inspections. Pollux test and measurement results were all acceptable. Pollux is expected to go to U1A in November. Pu Sustainment no longer has any obligations associated with the Gemini experiment.
- 2) Presented to (b) (6) on the successful assembly of the Pollux experimental device as part of the Gemini series.
- 3) Supported the release of the FY13 Pu Sustainment Program Implementation Plan.
- 4) Established the FY12 program baseline and allocated funds accordingly.
- 5) Meetings
 - a. Hosted the Pu Sustainment 4th Quarter Program Review
 - b. Hosted the Power Supply PRT
 - c. Traveled to KCP for the W87 Pit IPT

All four MRT L2 Milestones (4622-4625) associated with Plutonium Sustainment are on track for success in FY13.

The earned value metrics overall for LANL are within acceptable thresholds, so no high-level recovery plan is required.

Each of the four major LANL WBS elements is discussed in detail below with two sections at the end that are provided by KCP and LLNL.

Table 1: October Baseline Change Requests

WBS	BCR #	BCR Description	Date Assigned	Date Approved	Impact	Cost Impact	Change Level
Power Supply	PSM-12-058	Conduct MSA	9/17/12	Working	Cost/Scope	\$94k	3
Pu Sustainment	PSM-13-001	Establish FY13 Baseline	10/1/12	N/A	N/A	N/A	N/A
Power Supply	PSM-13-002	Temporary Lights, Concrete Samples and Door Modifications	10/1/12	10/1/12	Cost/Schedule	\$24k	3
Power Supply	PSM-13-003	Panel Board & AC Unit curb	10/1/12	10/18/12	Cost/Schedule	\$79k	3
Power Supply	PSM-13-005	Rate Adjustment	10/15/12	10/22/12	Cost/Schedule	TBD	3


A note about cost variances:

Historically, earned value and cost variance reporting has not been done in October. Providing these reports in the first month of the fiscal year has revealed two accounting system flaws. Firstly, "Level Of Effort" activities are planned and earned from the start of October and do not include the first week of the fiscal year (the week of September 24). So a 4-week LOE activity has 3 weeks of planned and earned value but 4 weeks of costs giving those activities a cost variance of -33% (CPI = 0.75). The second is that cost corrections do not happen retroactively but are reconciled in the month that the correction occurred. For example, an incorrect charge in October corrected the following month will show as a negative cost in November. These two factors have a large relative impact in early months and have resulted in a -15% cost variance in pit development (CPI = 0.87). When the cost corrections and LOE anomaly are factored out, the variance is +5% (CPI = 1.06). These problems have little impact on schedule variance reporting.

Earned Value Metrics


PERFORMANCE S-CURVE

Pu Sustainment

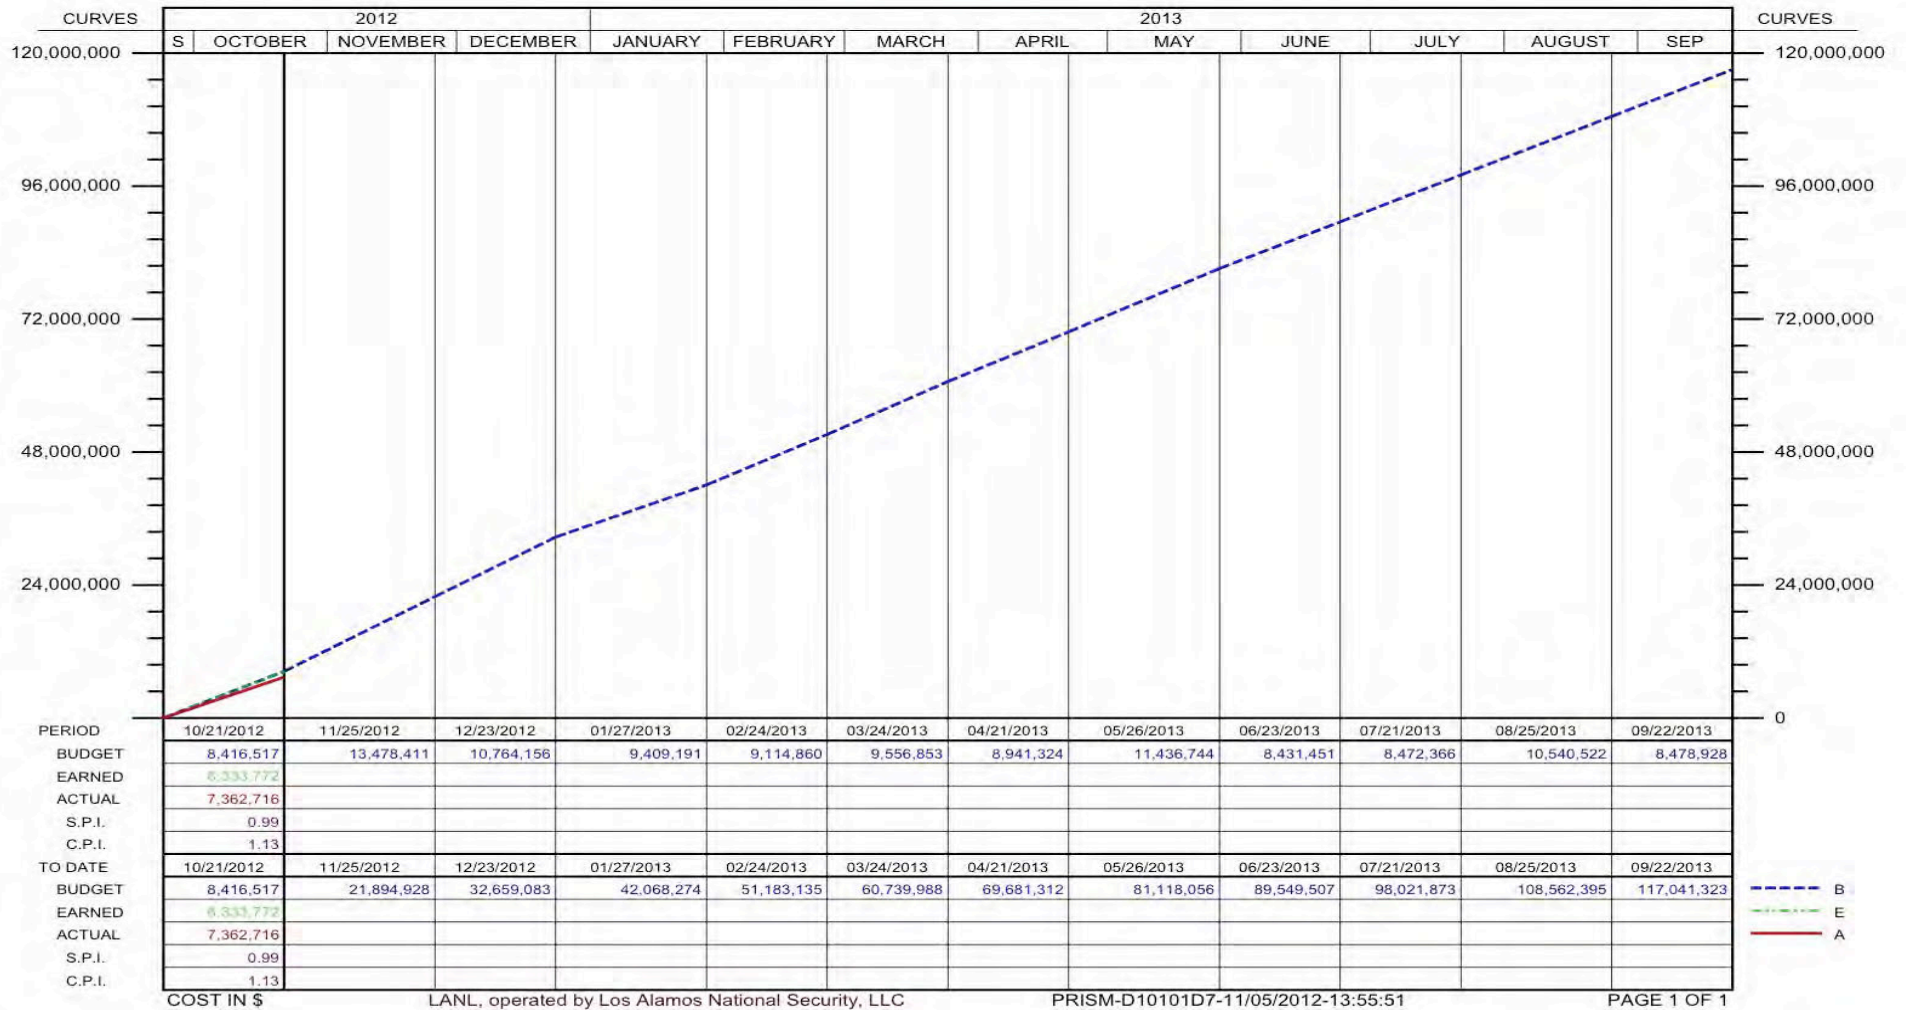

PERFORMANCE S-CURVE

Pu Sustainment W/O Facility Infrastructure

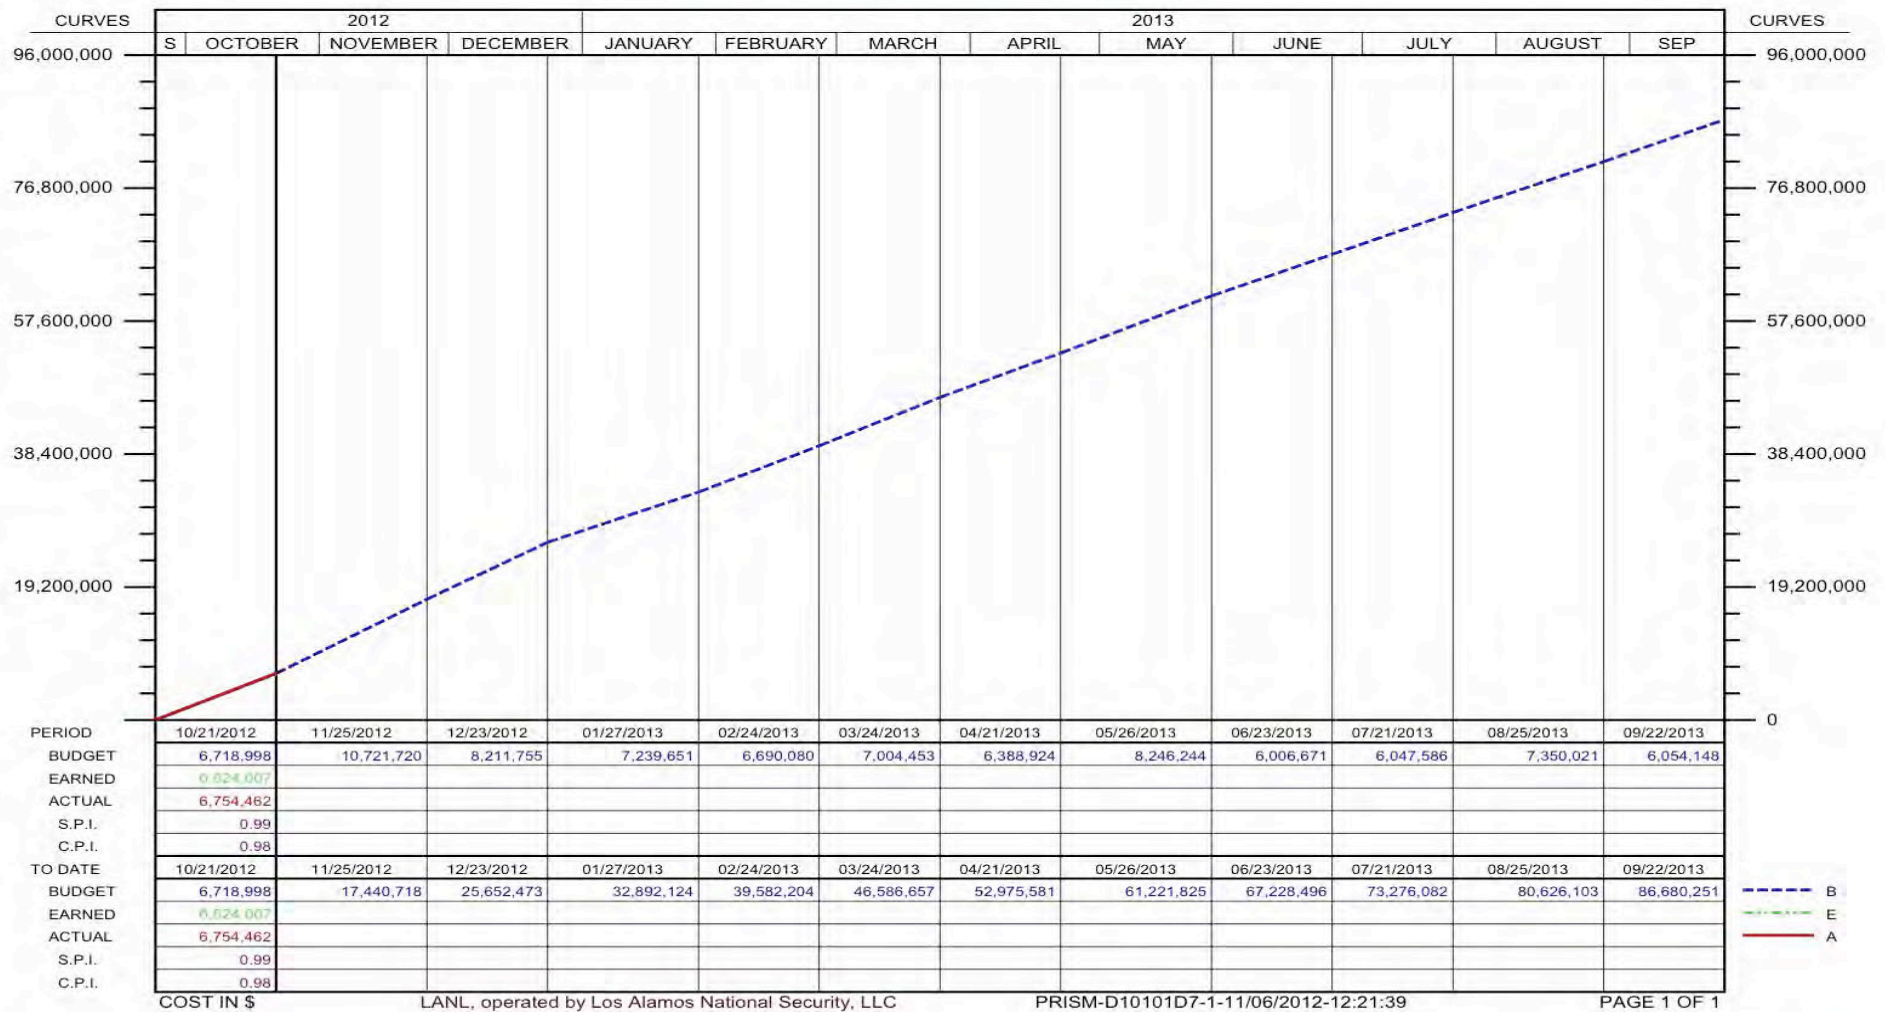

1.0 LANL - Pit Development

MRT 4622		GREEN	Perform Activities to Sustain Base Pit Material Processing and Fabrication Capability		
1. (b) (7)(F)					
2. Maintain pit manufacturing capability by producing (b) (7)(F) and/or exercising the pit fabrication flow sheet.					
3. Continue to make progress on the Electro-Refining line, Plutonium Foundry, and (b) (7)(F) projects.					
Builds	Baseline Date	Status/Comments	Completion Date	RGYB	
(b) (7)(F)				BLUE	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	
				GREEN	

1.1 Technical Progress

- Completed the drill and press operation successfully on the (b) (7)(F). Welding is schedule for early November.
- Completed producing three of three planned ER rings.
- Completed ahead of schedule all (b) (7)(F) **planned for first quarter.**
- Completed one shape casting as planned.
- Started BCR planning for (b) (7)(F) to take data in FY13. Due 12/21/12

1.2 Equipment

- The plan to meet the grading criterion #3 for L2 milestone MRT 4622 includes the following:
 1. The L (b) (7)(F) - complete all planned (b) (7)(F) upgrades and release both the “cold” and “hot” glovebox for welding operations by September 30, 2013.
 2. The Plutonium Foundry Upgrades - complete cold testing, issue an approved design for construction, and start construction on the first of three foundry gloveboxes by September 30, 2013.
 3. The Electro-Refining Upgrade - complete all mechanical and electrical construction activity associated with the eleven electro-refining boxes and systems by September 30, 2013.
- (b) (7)(F)
 - o Wiring of the switch and junction boxes continued
 - o Design of the (b) (7)(F) end panels was completed and is in procurement
 - o Evaluated encoder replacement options for PF-4
- Electro-Refining Line Upgrade
 - o Started equipment installation (construction) activities
 - o Continued procurements from the consolidated bill of materials (CBOM) necessary for installation
 - o The Laboratory Integrated Stewardship Council (LISC) approved the engineering support contract
- Foundry Upgrade
 - o Continued assembly of the cold test foundry
 - o Received Limited Volume Circulating Chilled Water system skid

1.3 Issues

- None

1.4 Variance Analysis and Recovery Plan

- None


1.5 BCRs

- None

1.6 Earned Value Metrics

PERFORMANCE S-CURVE

Pit Manufacturing

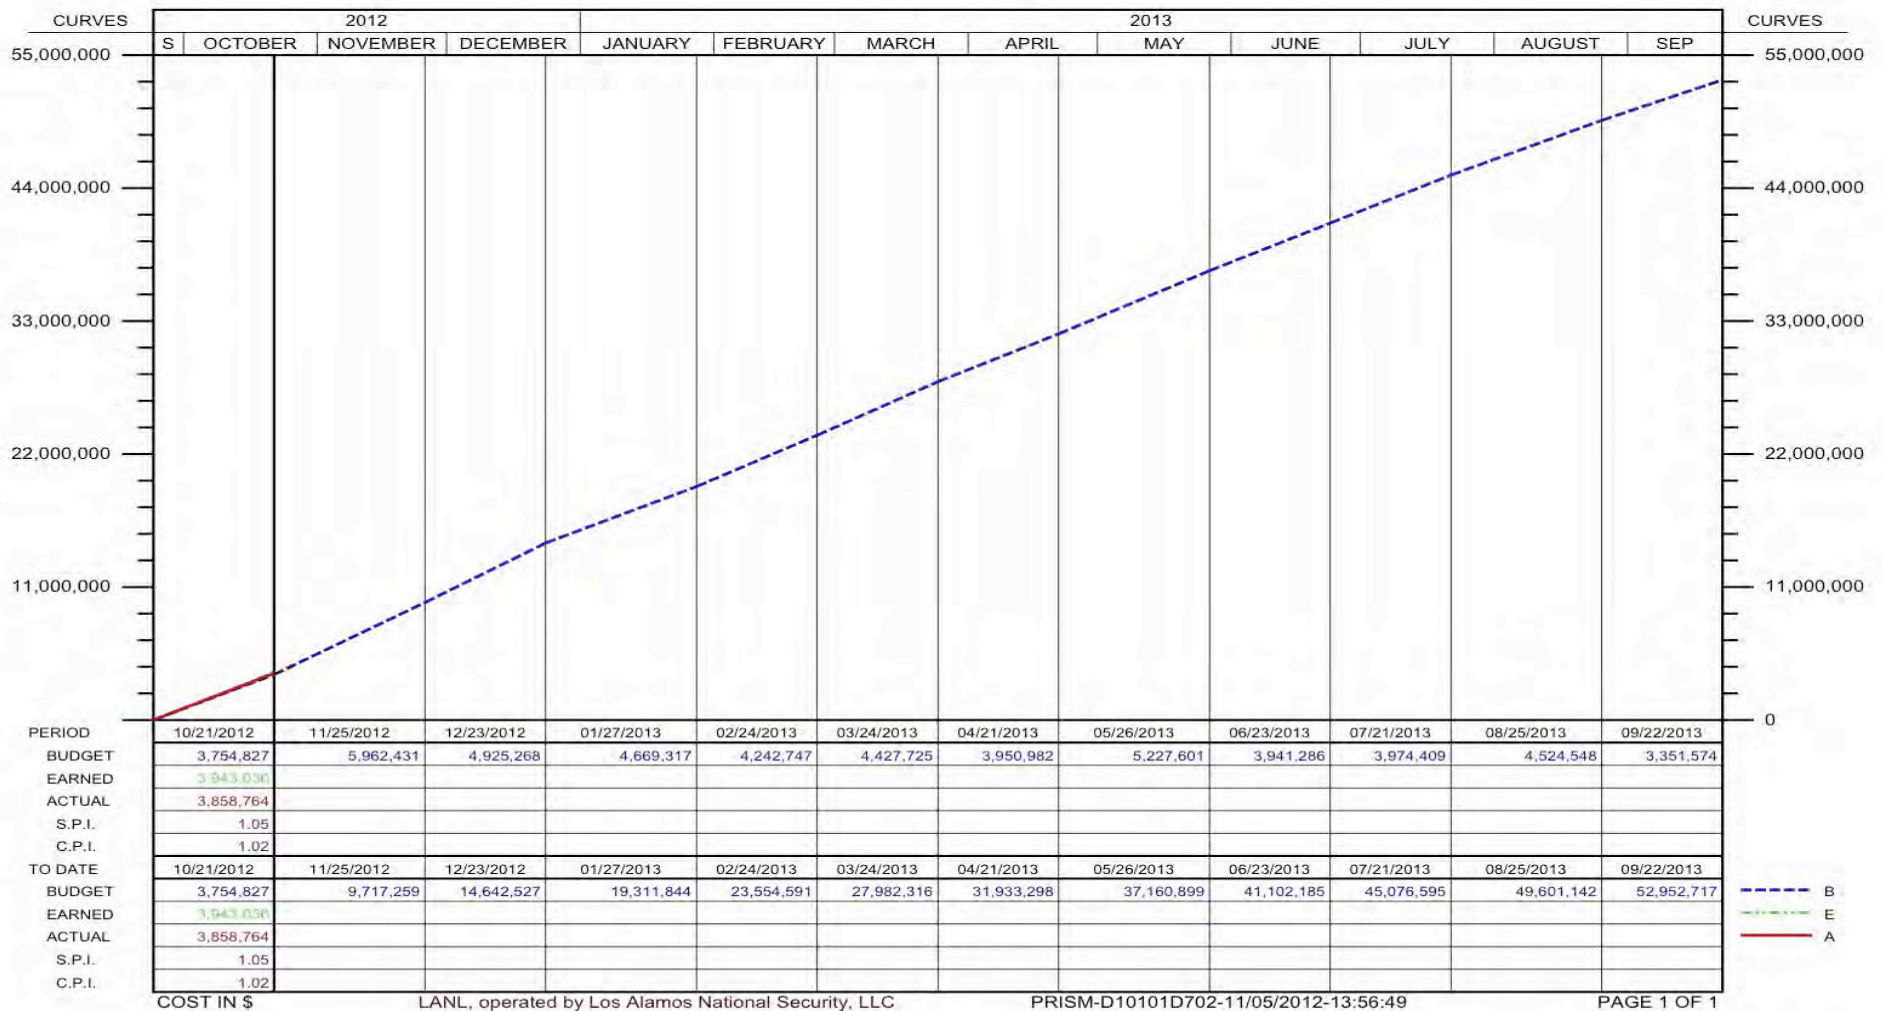

2.0 LANL - Power Supply

MRT 4624		GREEN	Install the RTG PSAA equipment and upgrades		
(b) (7)(F)					
L3/L4 Milestone	Baseline Date	Status/Comments	Completion Date	RGYB	
(b) (7)(F)					
MRT 4625		GREEN	Complete FY 2013 RTG material recovery activities		
1. Dismantle 95% of the Pantex items received by June 30, 2013 (up to 450 items)					
2. Recover and store the oxide by September 30, 2013.					
L3 Milestone	Baseline Date	Status/Comments	Completion Date	RGYB	
Fuel Recovered & Stored – July 2012 Shipment	October 16, 2012		September 12, 2012	BLUE	
Fuel Recovered & Stored – August 2012 Shipment	November 8, 2012			GREEN	
Fuel Recovered & Stored – November 2012 Shipment	February 6, 2013			GREEN	
Fuel Recovered & Stored – January 2013 Shipment	April 17, 2013			GREEN	
Fuel Recovered & Stored – March 2013 Shipment	June 11, 2013			GREEN	
Fuel Recovered & Stored – May 2013 Shipment	August 13, 2013			GREEN	
Fuel Recovered & Stored – June 2013 Shipment	September 3, 2013			GREEN	

2.1 Technical Progress

- **Material Recovery**
 - Received FY13 Shipment #1 and #2 (received in July and August, respectively).
 - All units from both shipments are dismantled.
 - Completed fuel recovery and storage of Shipment #1 in FSOs.
 - Completed fuel recovery and storage of Shipment #2 in FSOs. (b) (7)(F) delayed due to equipment failure. (b) (7)(F) is scheduled to resume in early November.
 - Received FY13 Shipment #3 on October 22, 2012.
- **RTG Process Development**
 - The PRT met October 17-18, 2012, at LANL. Tours of PF-5 and SM39 were made. The topics discussed included availability of the (b) (7)(F) bar and the acceptance of the material, a QA update, an Analytical Chemistry update, an E-Tester update, a schedule review, a materials and (b) (7)(F) a Design of Experiments discussion, a review of the Marlow component, and preparation for the November 13, 2012 Conceptual Design Review at SNL.

- o Preparing for updates of the LANL and KCP Production Strategies.
- o Continuing weld studies. SNL brought a 4-foot (b) (7)(F) for our use in preparing parts. The bar was sent to the manufacture for UT and Dye Penetration analysis.

2.2 Equipment

- Power Supply Assembly Area (PSAA)
 - o Construction continues and is on track.
 - o Completed a walk-down with the masons on core drilling for pipe pass through, exhaust head openings, and filling in the old exhaust fan openings.
 - o Completed placing asphalt along Beta Drive.
 - o Completed GPR for anchoring and fan installation.
 - o Completed installation of jib crane.
 - o Completed installation of exterior equipment platform steel.
 - o Continued installation of electrical raceway and service conductors.
 - o Continued layout of the vacuum exhaust header in the shock tower area.
 - o Continued installing the ventilation exhaust header.
 - o Continued painting beams and columns of equipment platform steel.
 - o Continued installing the building hot supply and return to the VAV boxes.
 - o Continued to insulate the building piping and fire stop the penetration in fire rated walls.
 - o Started installation of handrails for the equipment canopy.
 - o Started backfill and compaction around the transformer pad.
 - o Started installation of electrical panels PP-2 and PP-B.
- The (b) (7)(F)
 - o Completed vendor setup and LANL SME training.
 - o Continued preparation for LANL MSA.
- Analytical Chemistry glove boxes (Pu Assay and Radiochemistry)
 - o Completed Radiochemistry box connection to drop box.
 - o Completed installing Radiochemistry box on GB legs.
 - o Prepared the Zone 2 ductwork for installation.
 - o Continued mechanical bulk installations.
 - o Completed LISC approval for Merrick Title III effort.
- SM-39 Development Laboratory
 - o Continued electricity installation for process equipment.

2.3 Issues

- None

2.4 Variance Analysis and Recovery Plan

- SPI - Progress deviated from planning basis due to equipment failure of the welding glovebox's oxygen analyzer and the Hytec radiography system, which have delayed (b) (7)(F). Overall, the milestone remains on track, despite the variance.
- Recovery Plan – Procurement of necessary parts for repair of equipment has been expedited. (b) (7)(F) is scheduled to be completed by the middle of November.


2.5 BCRs

- None

2.6 Earned Value Metrics

PERFORMANCE S-CURVE

Reconstitution of Power Supply Manufacturing

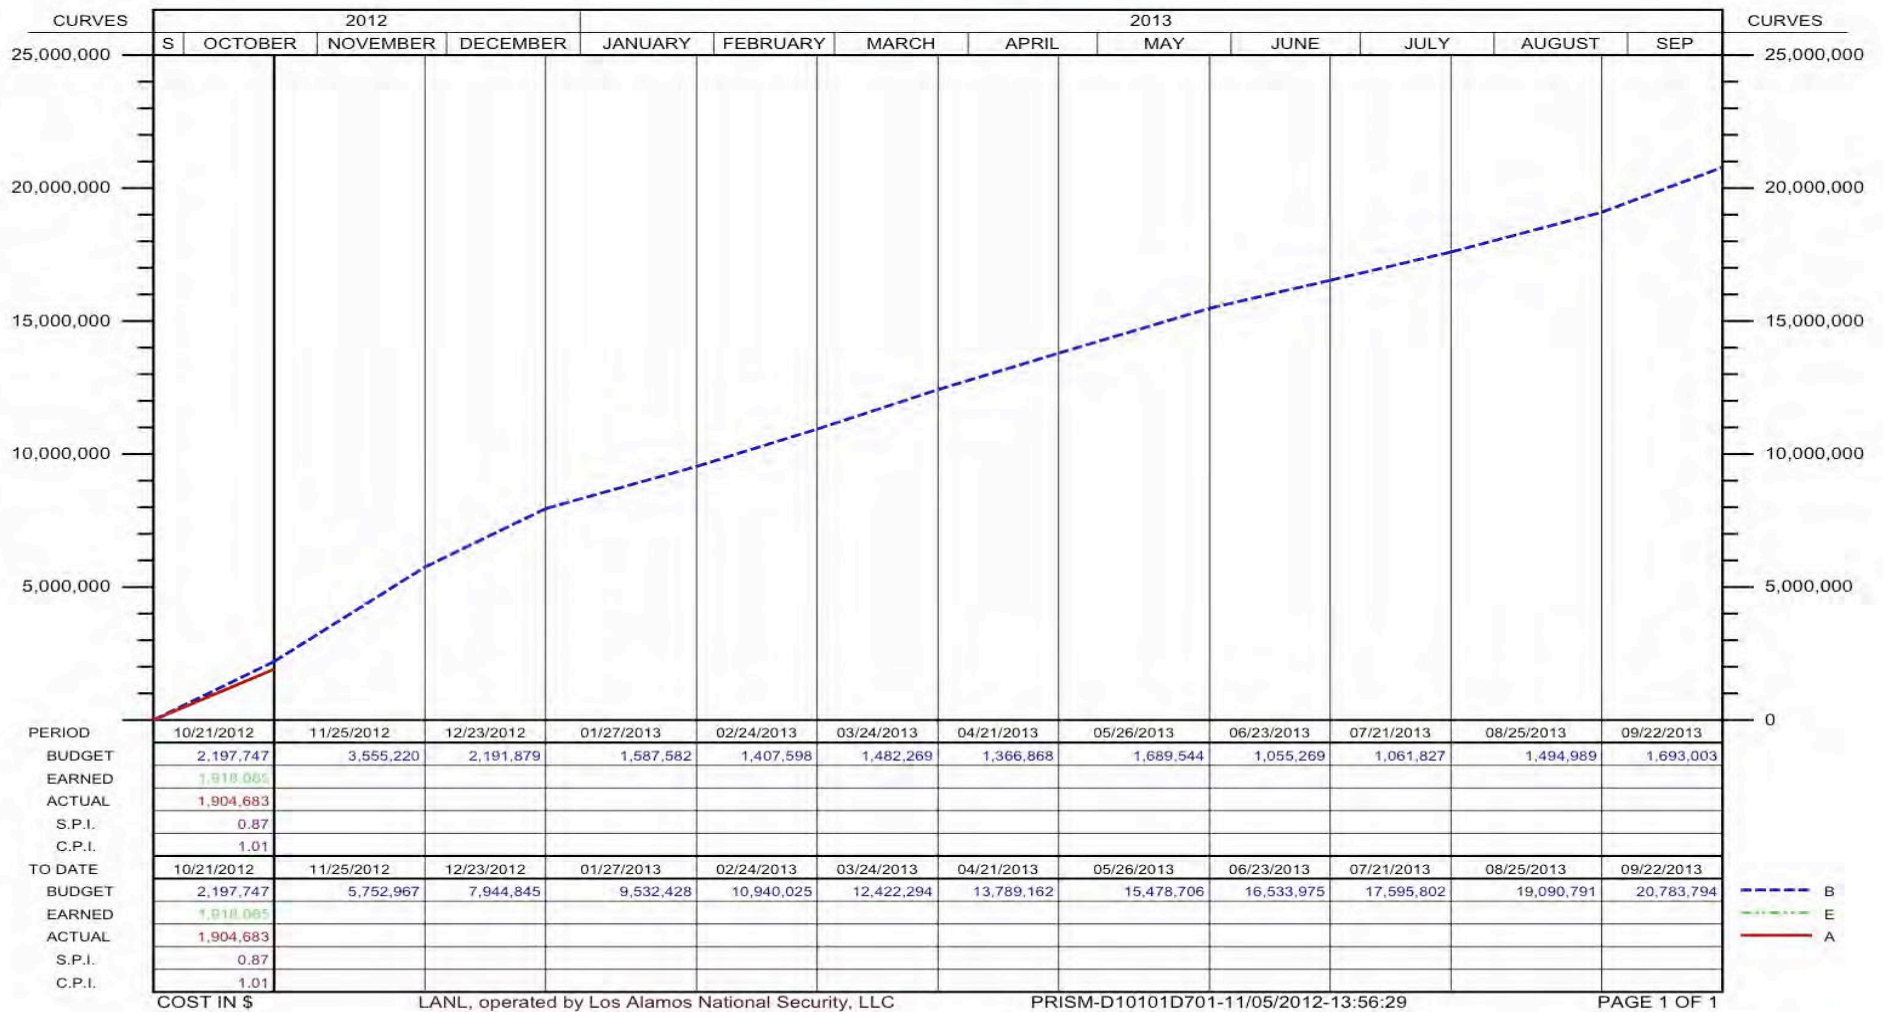

3.0 Program Management and Support

3.1 Program Management

- Completed and released FY13 baseline schedule, work packages, and allocation 0.1.
- Earned value and actual cost reporting are being tracking in October.

3.2 Support

- Progress on support functions will be reported beginning in November.

3.3 Issues

- None

3.4 Variance Analysis and Recovery Plan

- Cost variance is an artifact of the LOE accounting flaw (see executive summary). The impact of this accounting flaw will be diluted with each month but not fully reconciled until the end of FY13.


3.5 BCRs

- None

3.6 Earned Value Metrics

PERFORMANCE S-CURVE

Program Office

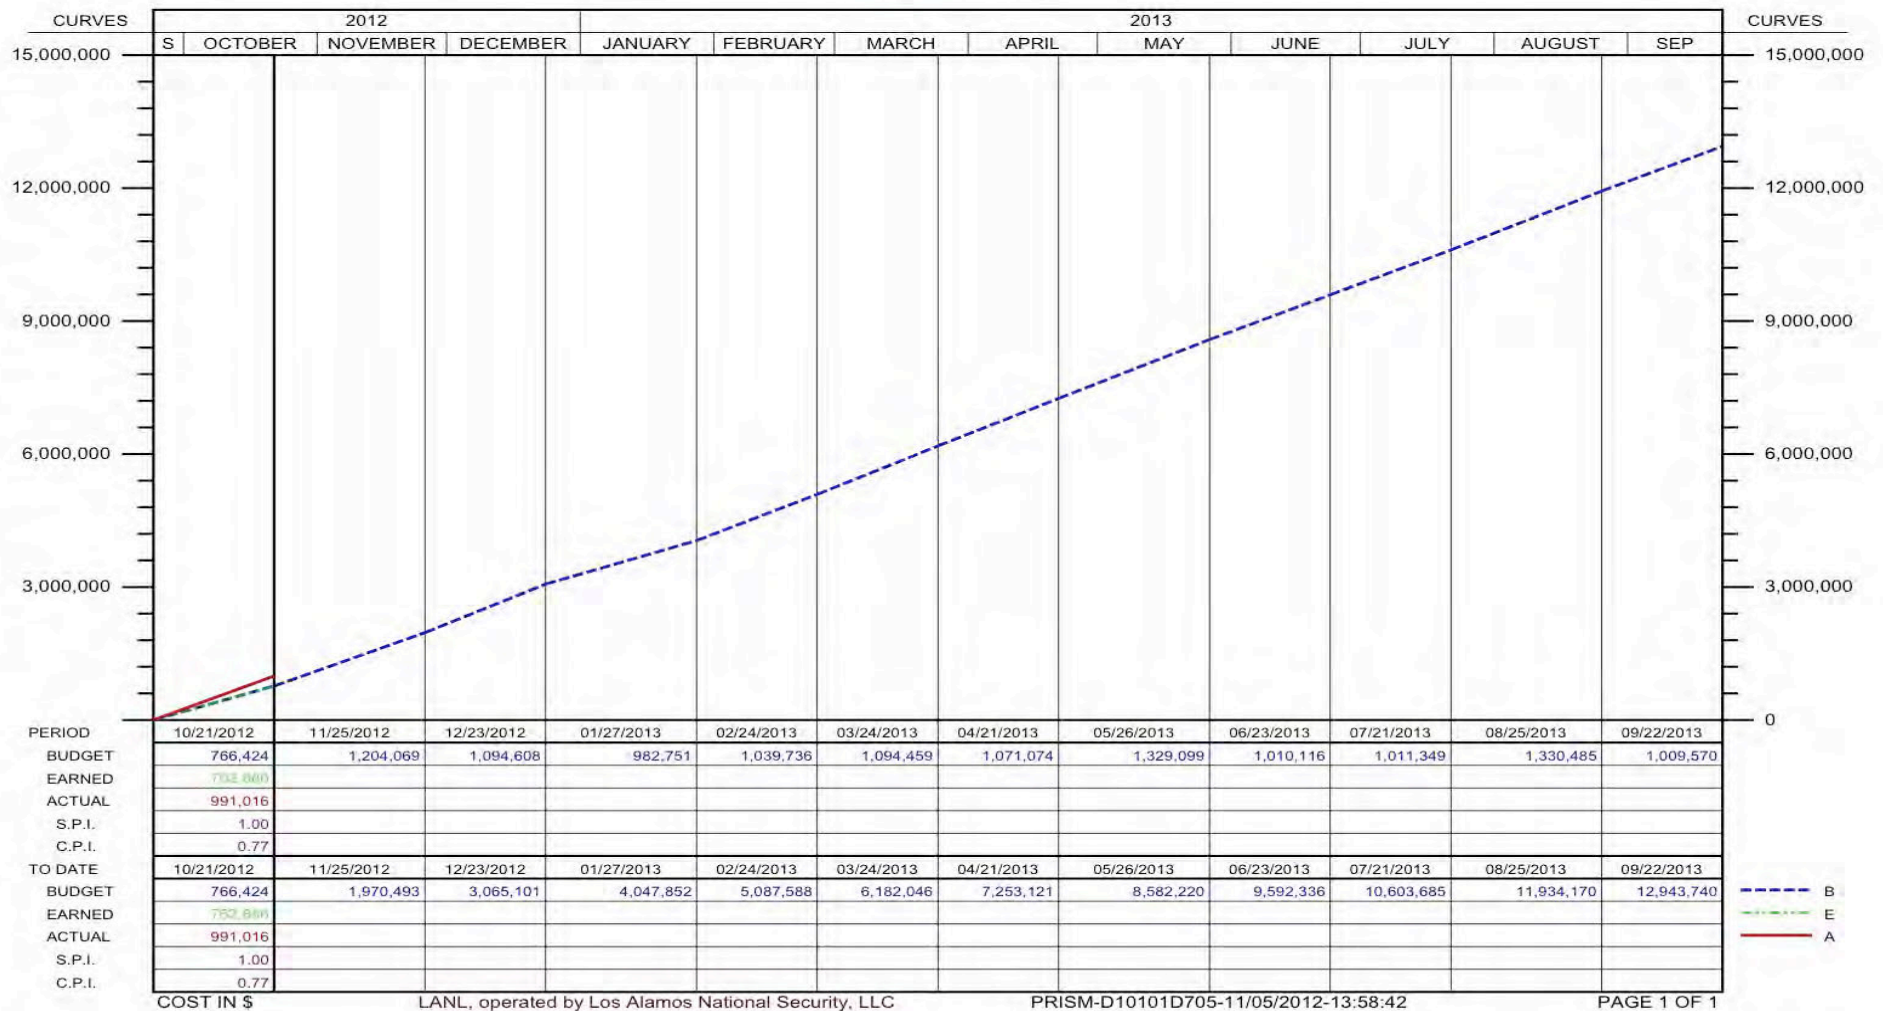

4.0 Facilities, Waste and Institutional Support

4.1 Technical Progress

- PF-4 Facility Availability: October N/A%
 - o 100 Area: N/A%
 - o 200 Area: N/A%
 - o 300 Area: N/A%
 - o 400 Area: N/A%

4.2 Equipment

- N/A

4.3 Issues

- N/A

4.4 Variance Analysis and Recovery Plan

- Note that the actual costs are well below the planned costs. This is an artifact of the monthly billing by RTBF. The costs came in after the financial end of the month. There is no concern at this time nor is there an expectation that this will under run and provide budget for other scope.


4.5 BCRs

- N/A

4.6 Earned Value Metrics

PERFORMANCE S-CURVE

Facility Infrastructure

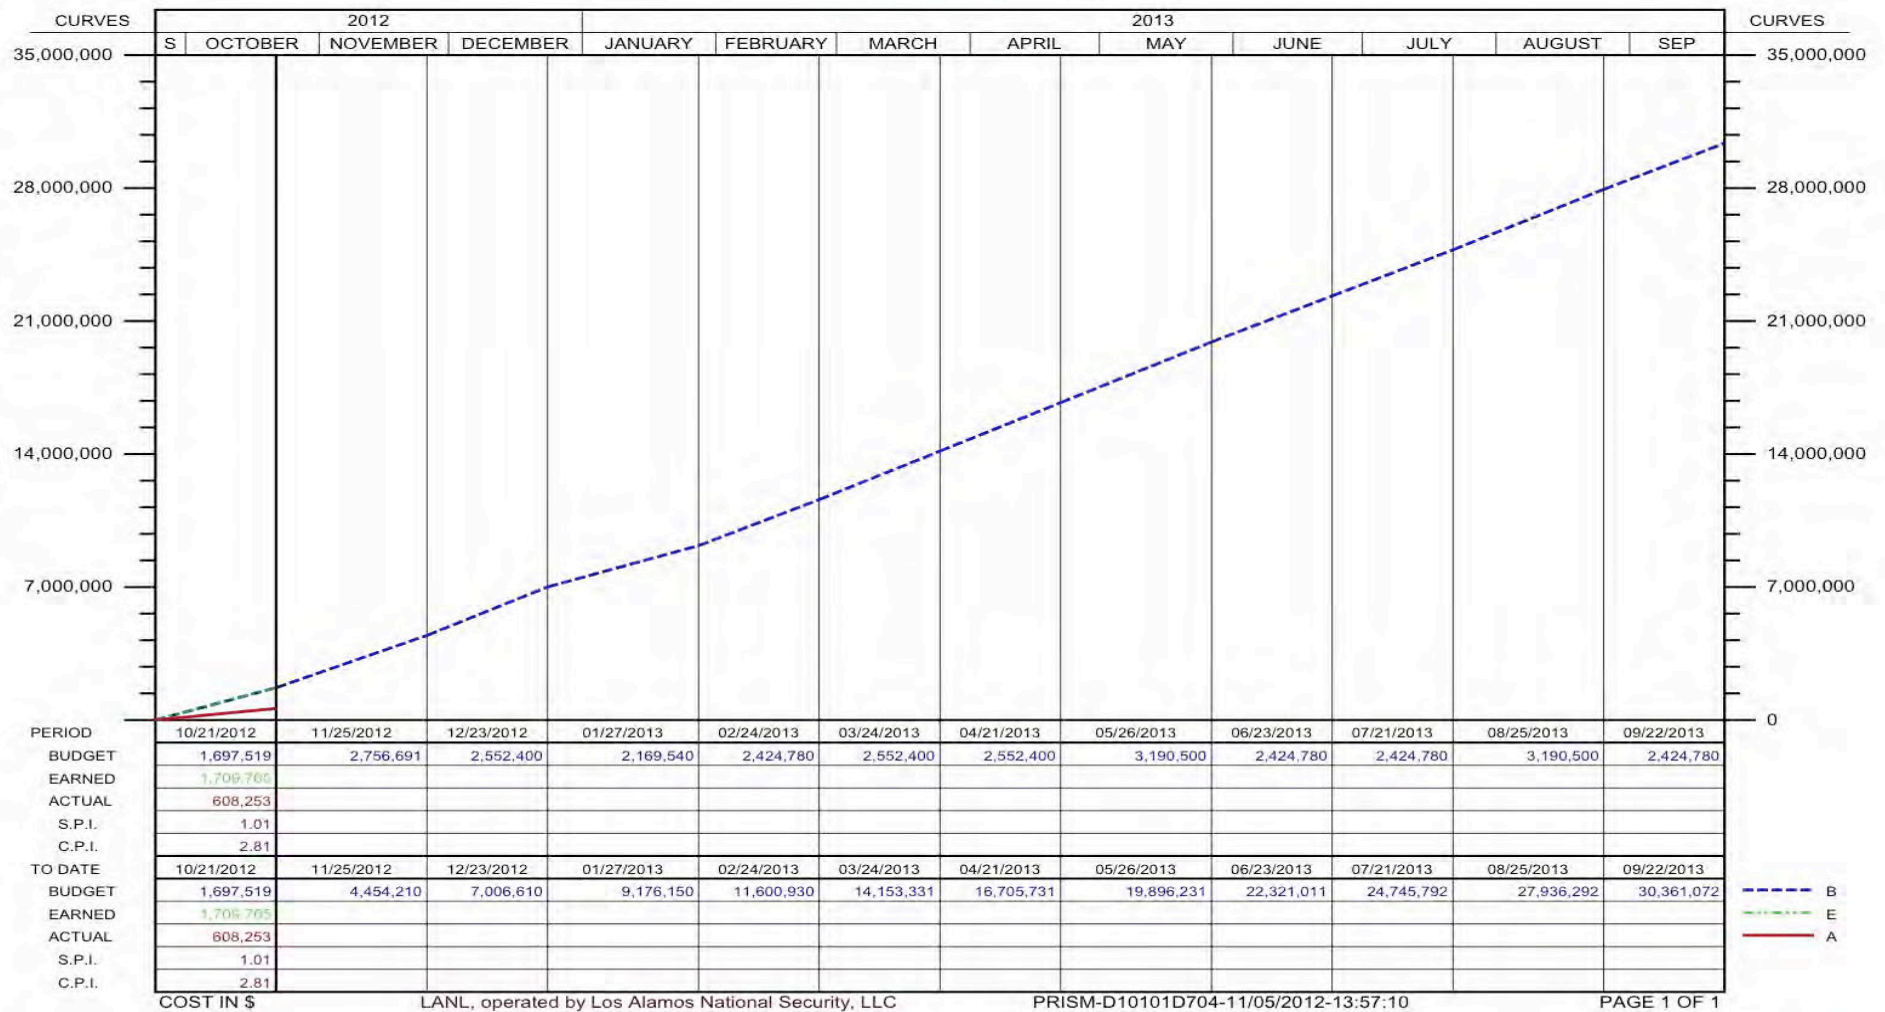

5.0 KCP

	GREEN	Begin Development of Non-Nuclear Component Manufacturing capability		
1. Purchase and install new (b) (7)(F) by 9/13				
2. Procure development material by 7/13				
3. Start fabrication of (b) (7)(F) by 8/13				
L2 Milestone	Baseline Date	Status/Comments	Completion Date	RGYB
Purchase and install new (b) (7)(F)	9/30/2013	2 ea. vendor visits complete. Pending receipt of response to RFQs		GREEN
Procure development material	7/31/13	Material Specification review		GREEN
(b) (7)(F)	8/31/2012	4th quarter FY13		GREEN

5.1 Technical Progress

- Input submitted to NNSA for PEP and Level II Milestones
- Engineering/program management team assembled
- ITP meeting held on Oct 10
 - Teaming – LANL/KCP/LLNL interfaces established
 - Initial material standards review
- Team sent to vendors as part of (b) (7)(F) purchase process
- Activity related to equipment placement at Botts Rd. I/W
- Meetings set up with LANL/LLNL to discuss material specifications

5.2 Equipment

- Two vendors have been visited – requests for quotes initiated – Pending final response

5.3 Issues

- None

5.4 Variance Analysis and Recovery Plan

- N/A

5.5 BCRs

- Work Authorization/Mission assignment received
 - BCR initiated establishing funding profile
- Project accounts set up and opened

5.6 Earned Value Metrics

- \$4.1M-Full Funding
- \$3.937M-Spend Plan
- \$1,901,115-MA
- As of end of October = \$47,156 Actuals

Graphical report will be initiated in November

6.0 LLNL

MRT 4749		GREEN	Perform Activities to Sustain Base Pit Material Processing and Fabrication Capability		
1.	(b) (7)(F)				
2.	In coordination with LANL PA, maintain (b) (7)(F) measuring device for process qualification				
3.	(b) (7)(F)				
4.	(b) (7)(F)				
5.	(b) (7)(F)				
L2/L3 Milestone		Baseline Date	Status/Comments	Completion Date	RGYB
(b) (7)(F)		9/30/2013			GREEN
(b) (7)(F)		7/30/2013			GREEN
Complete (b) (7)(F)		3/31/2013			GREEN
Initiate readiness review for compatibility tests		9/30/2013			GREEN
(b) (7)(F)					
Complete initial demonstration of purification and recovery of desired materials		6/30/2013			GREEN
(b) (7)(F)		12/31/2012	Design updated and initial DA review completed		GREEN
(b) (7)(F)		9/30/2013			GREEN

6.1 Technical Progress

- The pit production IPT met at Kansas City Plant on October 10th. The discussion primarily focused on preliminary KCP plans for the non-nuclear Mission and on answering KCP questions regarding design definition. Since the IPT meeting, the IPT DA has focused on reviewing design definition change requests and updating/adding drawings to reflect the new mission assignment.
- (b) (7)(F)
- (b) (7)(F)
- (b) (7)(F)

6.2 Equipment

- None

6.3 Issues

- None

6.4 Variance Analysis and Recovery Plan

- None

6.5 BCRs

- None

6.6 Earned Value Metrics

- \$6,980k planned FY13
- \$743k planned in October
- \$780k actual
- 11% complete

Graphical report will be initiated in November
